

Phase I Scope:

1. Move field operations into the food service building
2. Install perimeter fence and TESC measures
3. Demo and Abate the Science kit, Alt HS and South Windy Ridge House
4. Install Access Road to future middle school parking
5. Install Sewer re-route for middle school
6. Install main utilities south of food service building to the main building
7. Create lighted path along east fence line from transpo parking area to the existing high school.
8. Install temp access road to North Windy Ridge house

PHASE I
 June 2017 - Aug. 2017

Demo existing Alt. Middle School and adjacent structure and log trees. Area already fenced.

Lit Path for Student Walkway

North Windy Ridge Residence

Construction Perimeter Fence

Grade Building Pad and Start Foundations.

ATB Around Building Perimeter


Maintain Food Service bldg for Construction offices and temp secure storage

Primary Construction Entrance

Install access ramp from food services up to access road


Install West Side Detention Ponds


Secondary Construction Entrance

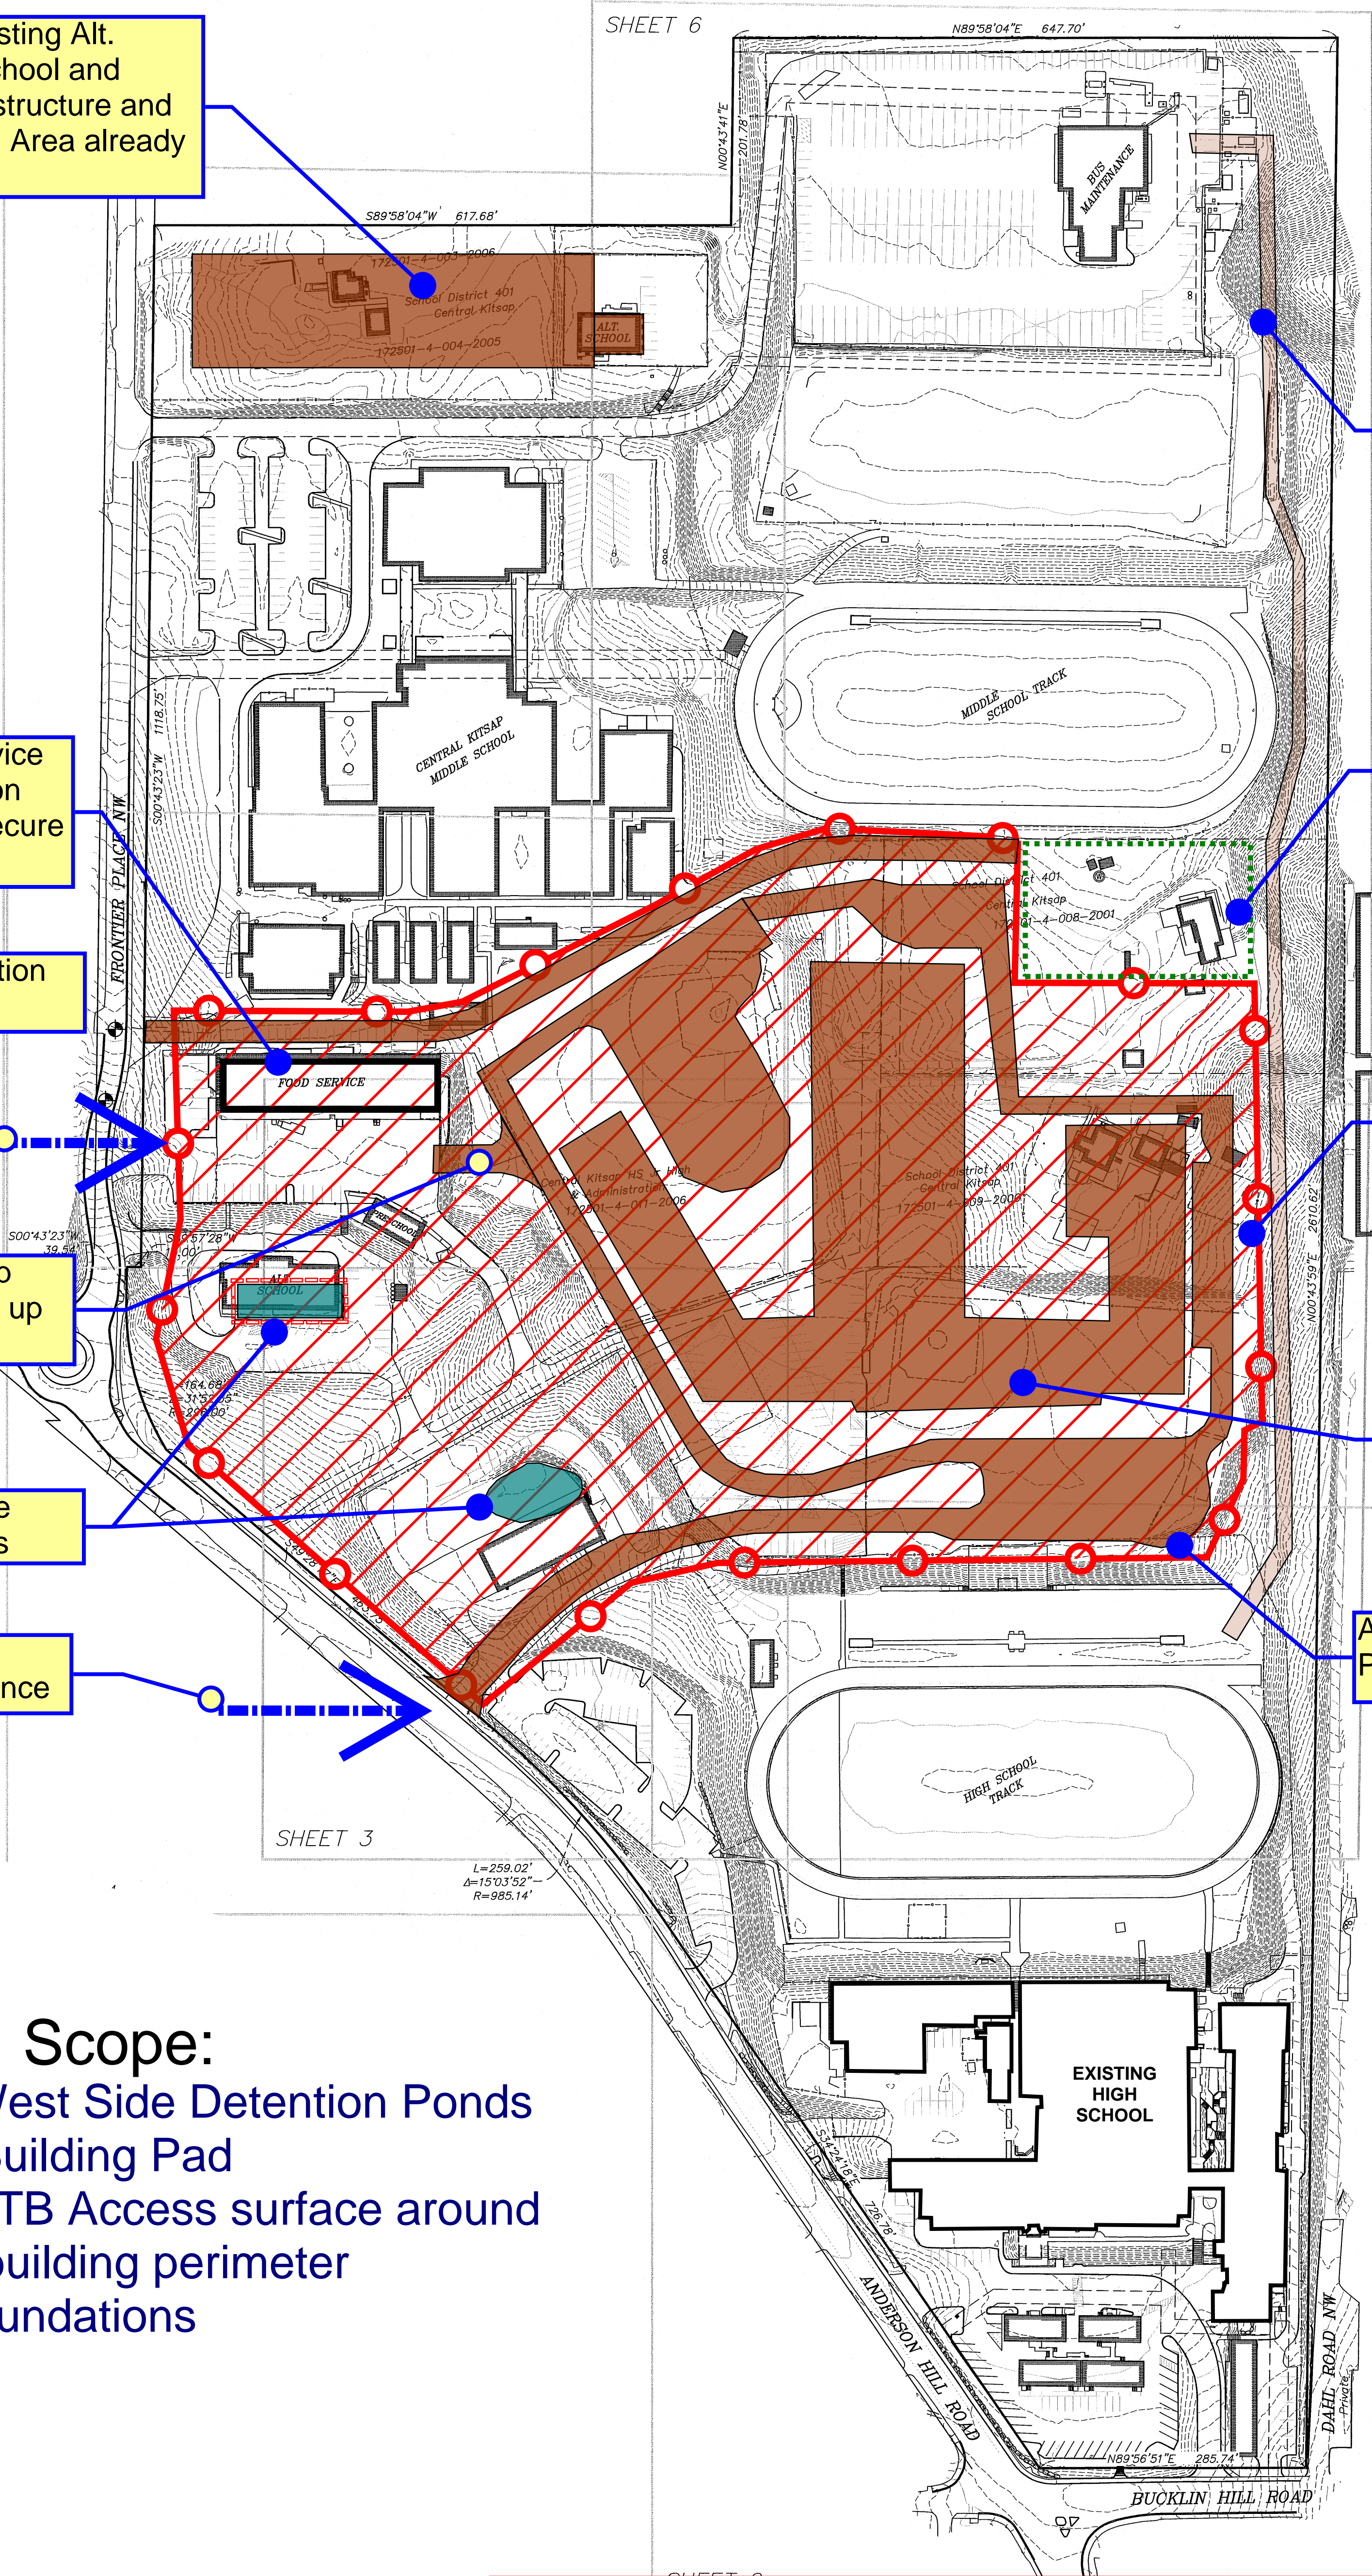

- Phase II Scope:**
1. Install West Side Detention Ponds
 2. Grade Building Pad
 3. Install ATB Access surface around complete building perimeter
 4. Start Foundations

PHASE II
Sept 2017 - Feb. 2018

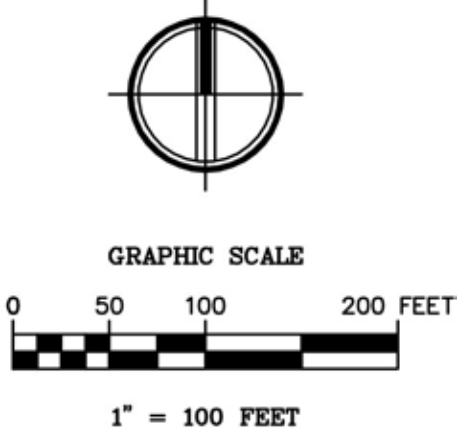

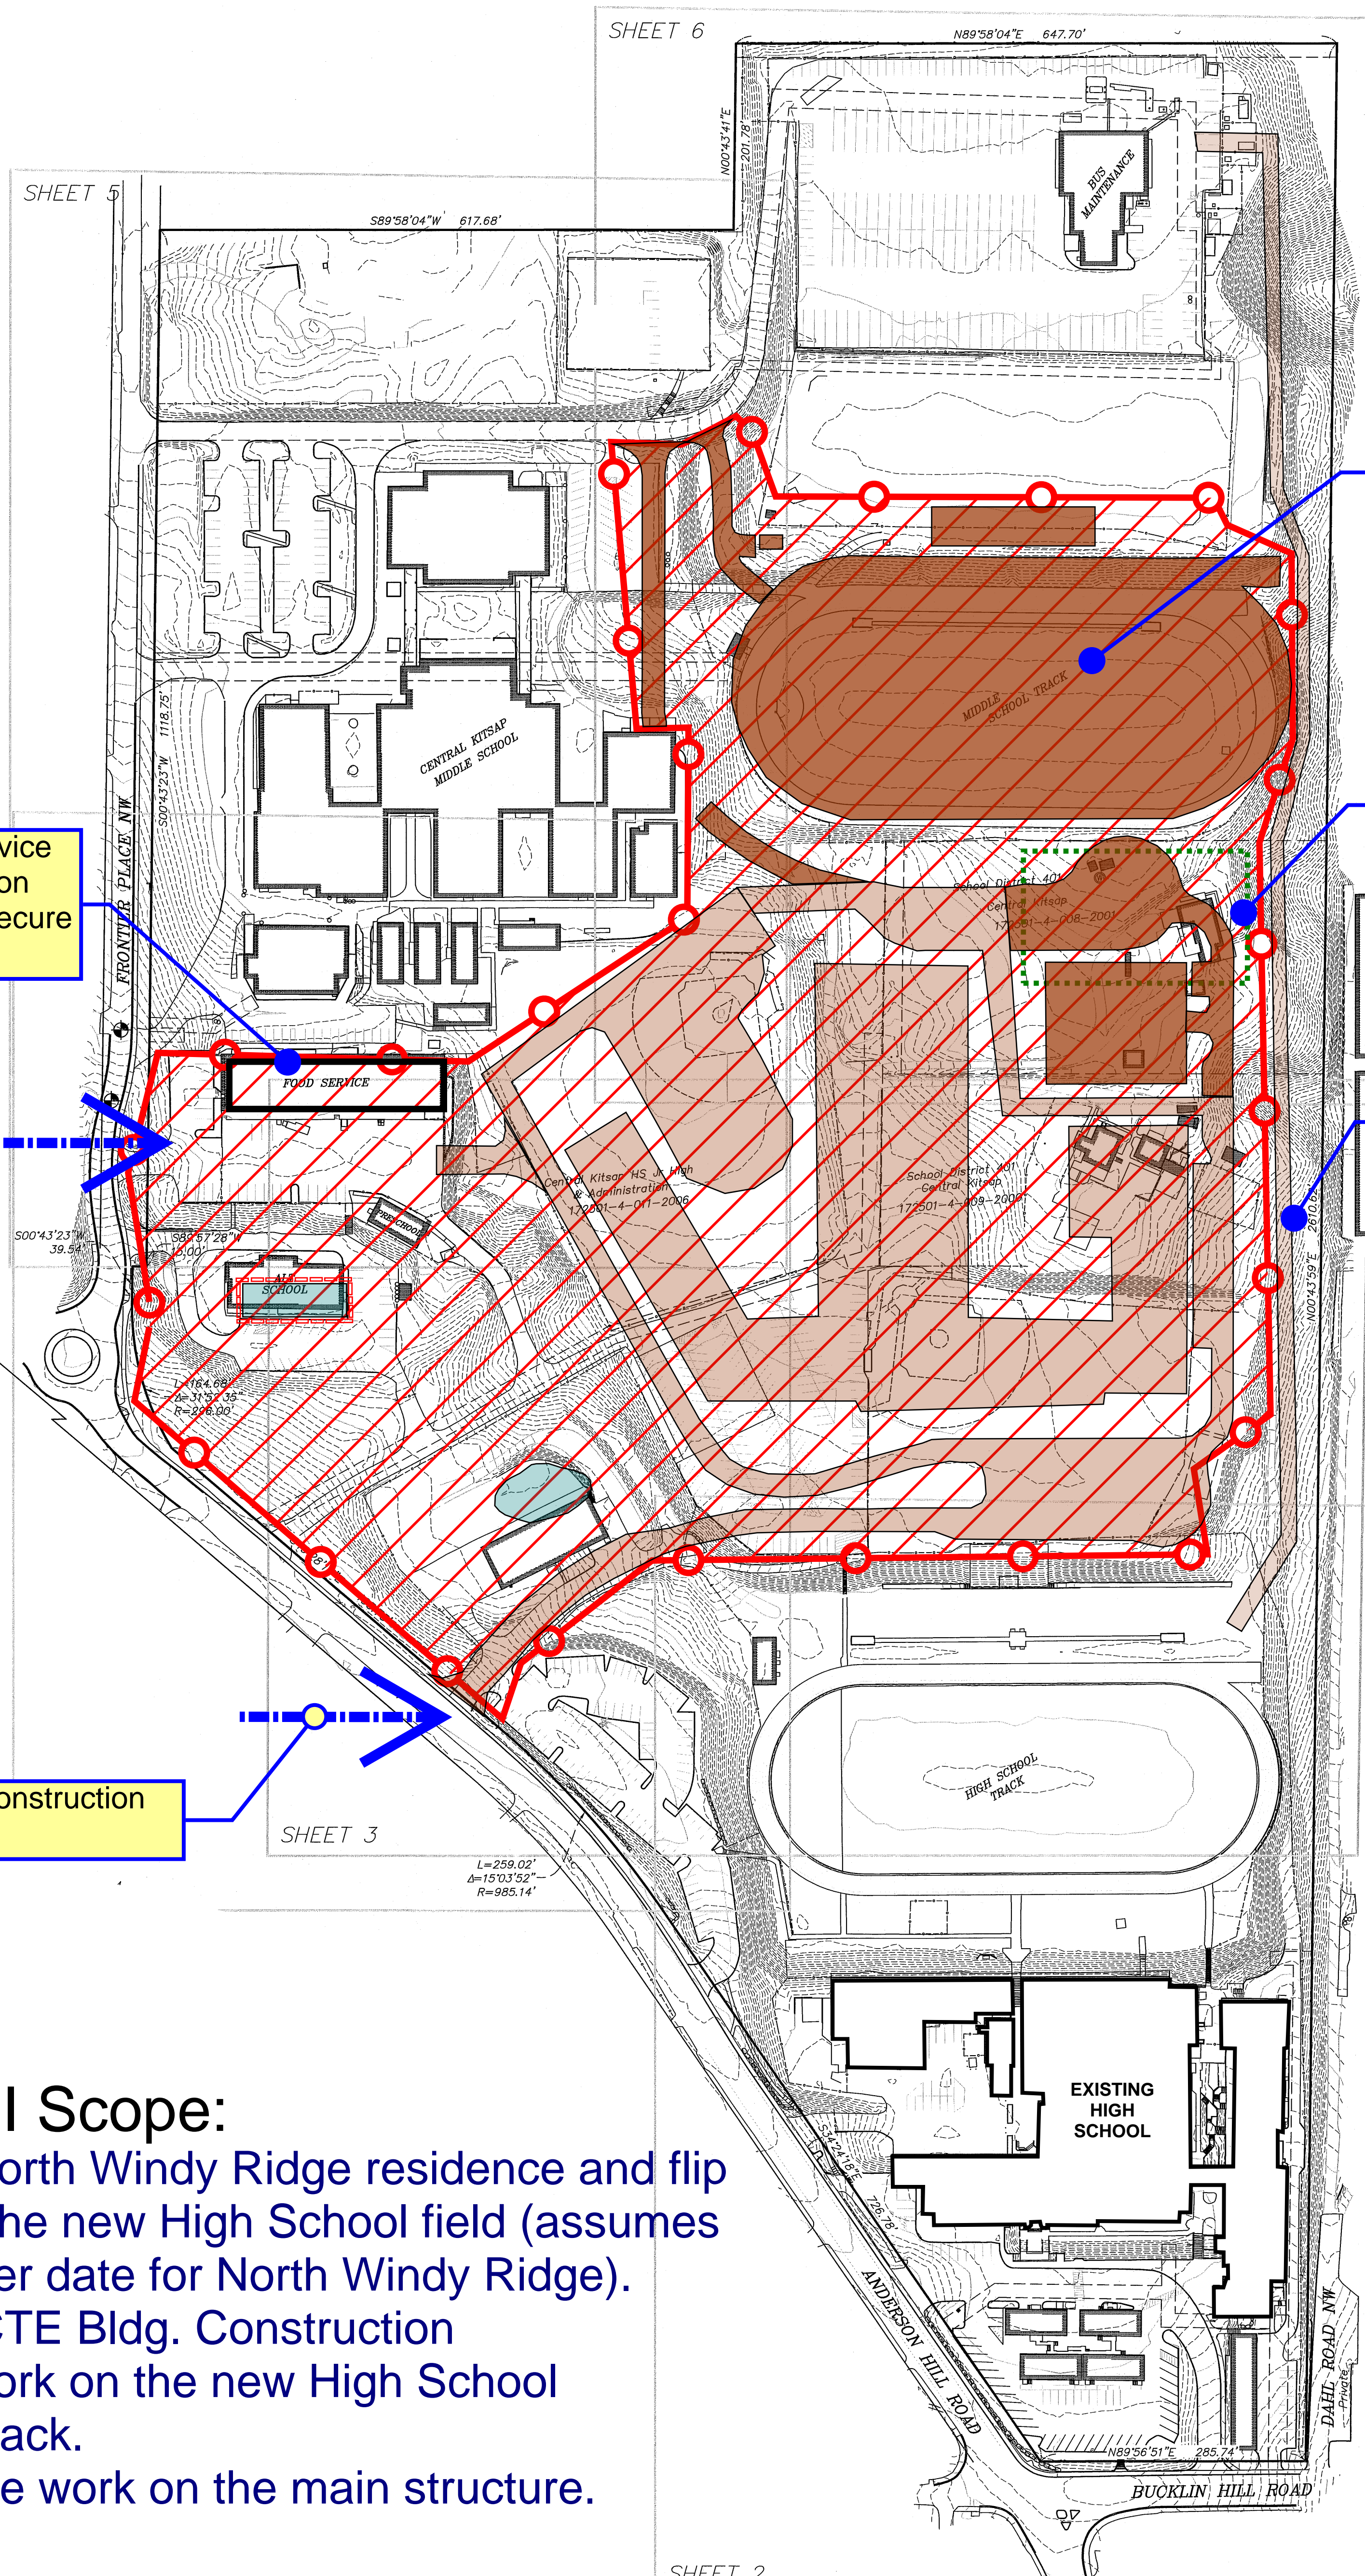

Rework existing Middle School field into new Synthetic Field Turf & Track.

Demo North Windy Ridge Residence and re-grade for CTE bldg.

Lighted High School Student access route


Maintain Food Service bldg for Construction offices and temp secure storage

Primary Construction Entrance

Phase III Scope:

1. Demo North Windy Ridge residence and flip soils onto the new High School field (assumes late turnover date for North Windy Ridge).
2. Begin CTE Bldg. Construction
3. Begin work on the new High School synthetic track.
4. Continue work on the main structure.

PHASE III
March 2018 - June 2018

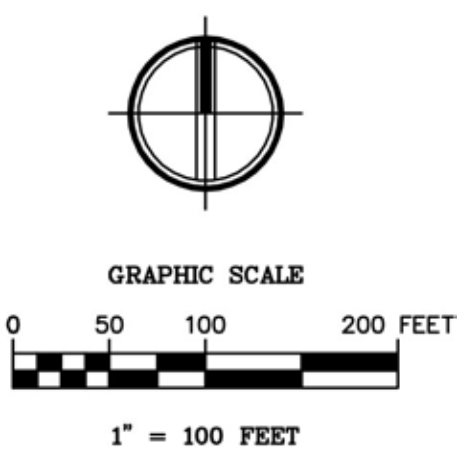

Install Tennis Courts and rework adjacent parking as needed. Area already fenced.

Demo Transpo Bldg. & associated UST's.

Finished new High School synthetic track & field available for use.

Construction Perimeter Fence


Rework Huey Field to new Configuration

Need to determine a way to align bus loop or reroute buses till after the Middle School is demolished.

Maintain Food Service bldg for Construction offices and temp secure storage

Secondary Construction Entrance


Primary Construction Entrance

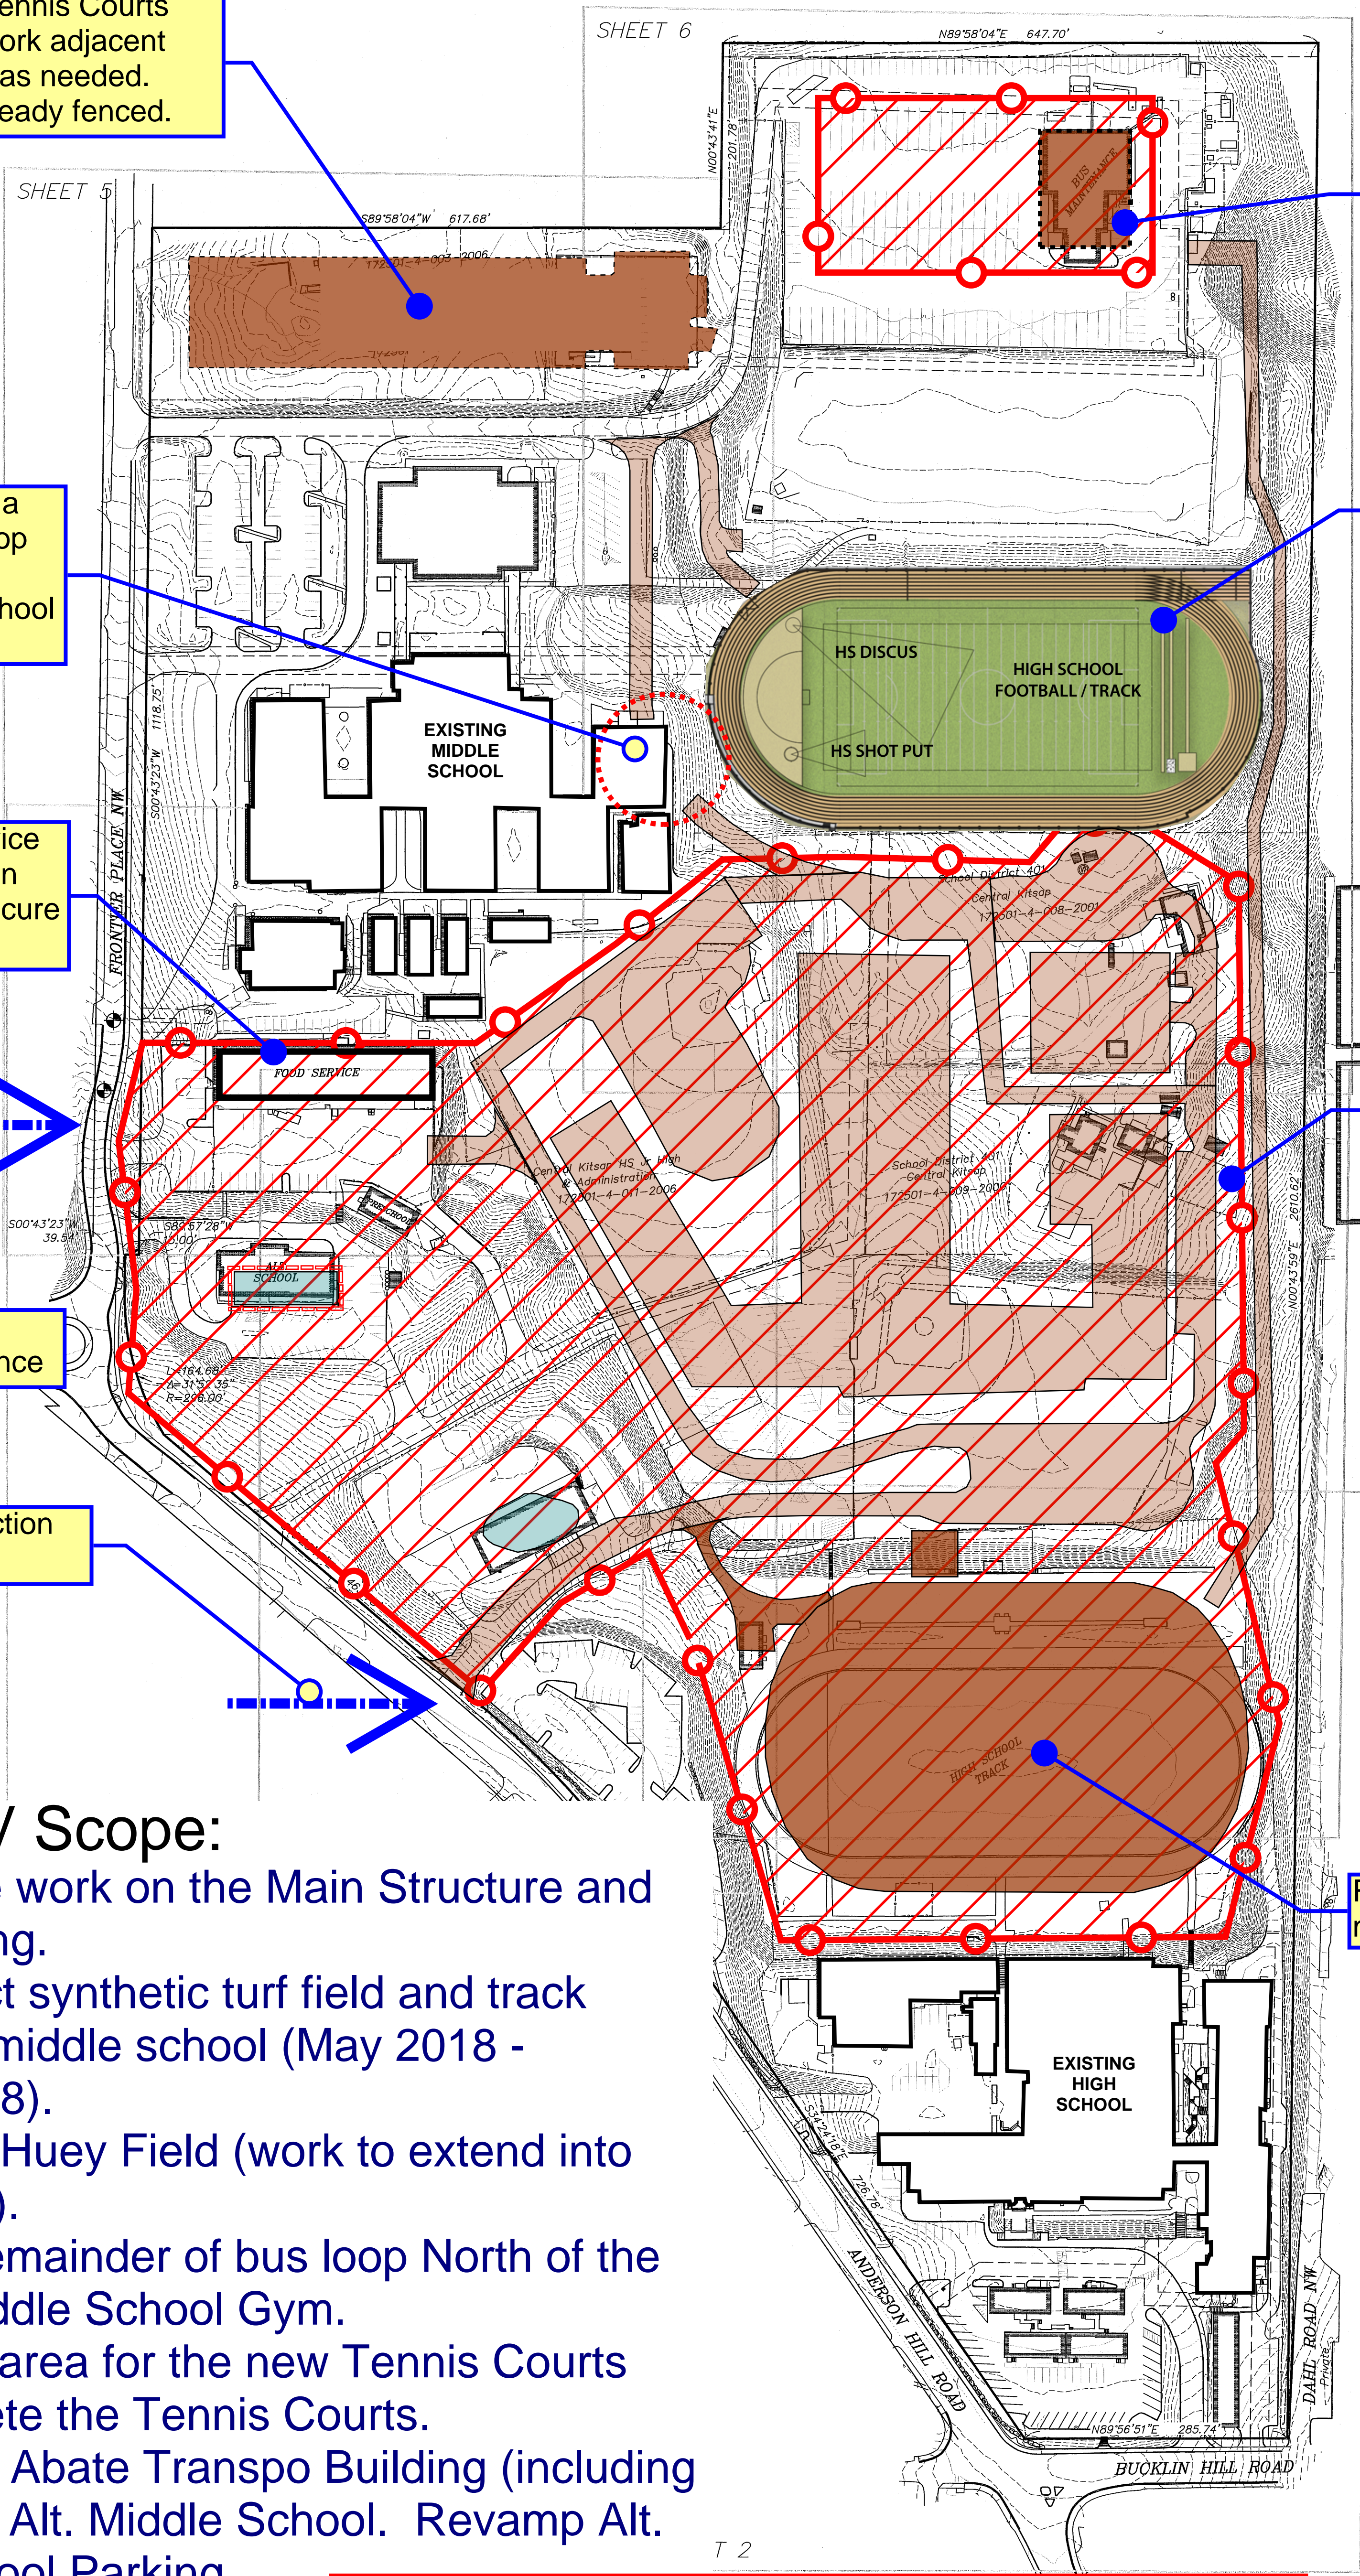

Phase IV Scope:

1. Continue work on the Main Structure and CTE Building.
2. Construct synthetic turf field and track at existing middle school (May 2018 - August 2018).
3. Rework Huey Field (work to extend into September).
4. Install remainder of bus loop North of the existing Middle School Gym.
5. Log the area for the new Tennis Courts and complete the Tennis Courts.
6. Demo & Abate Transpo Building (including UST's) and Alt. Middle School. Revamp Alt. Middle School Parking.

PHASE IV
July 2018 - Aug. 2018

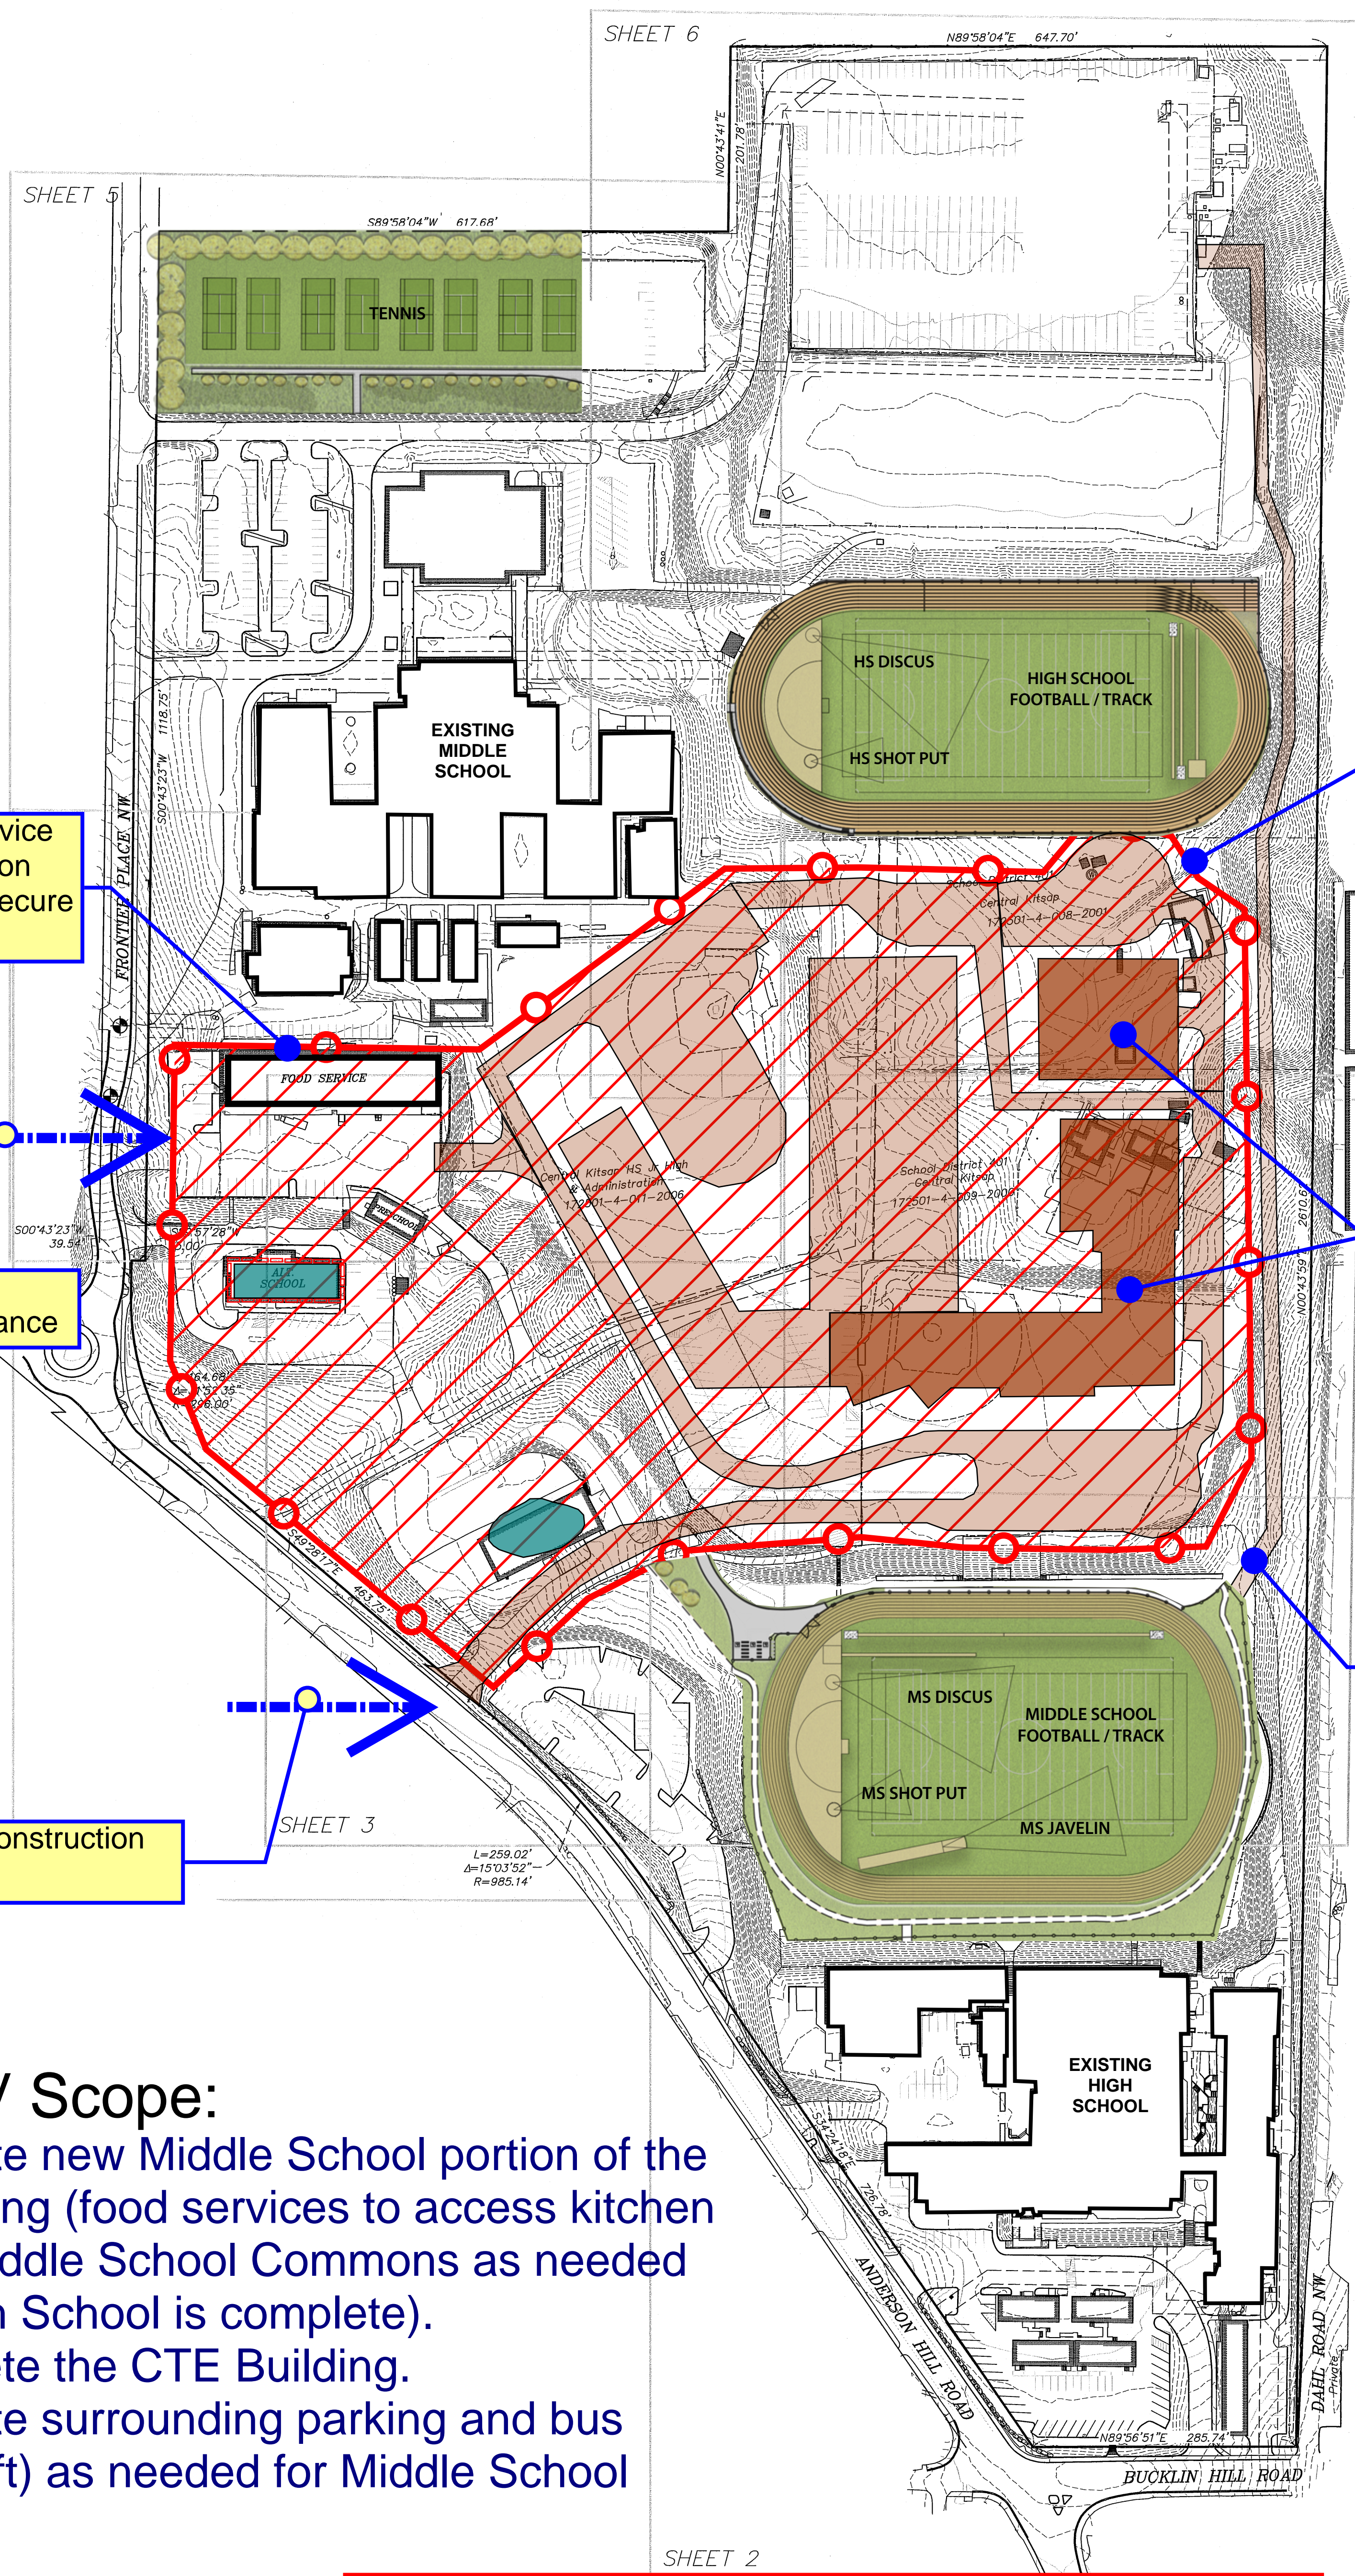

Maintain Food Service bldg for Construction offices and temp secure storage

Secondary Construction Entrance

Primary Construction Entrance

Construction Perimeter Fence


Finish Middle School portion of the main building and CTE building.

Lit Path for Student Walkway

Phase V Scope:

1. Complete new Middle School portion of the main building (food services to access kitchen through Middle School Commons as needed till the High School is complete).
2. Complete the CTE Building.
3. Complete surrounding parking and bus loop (top left) as needed for Middle School opening.


PHASE V
Sept. 2018 - Dec. 2018

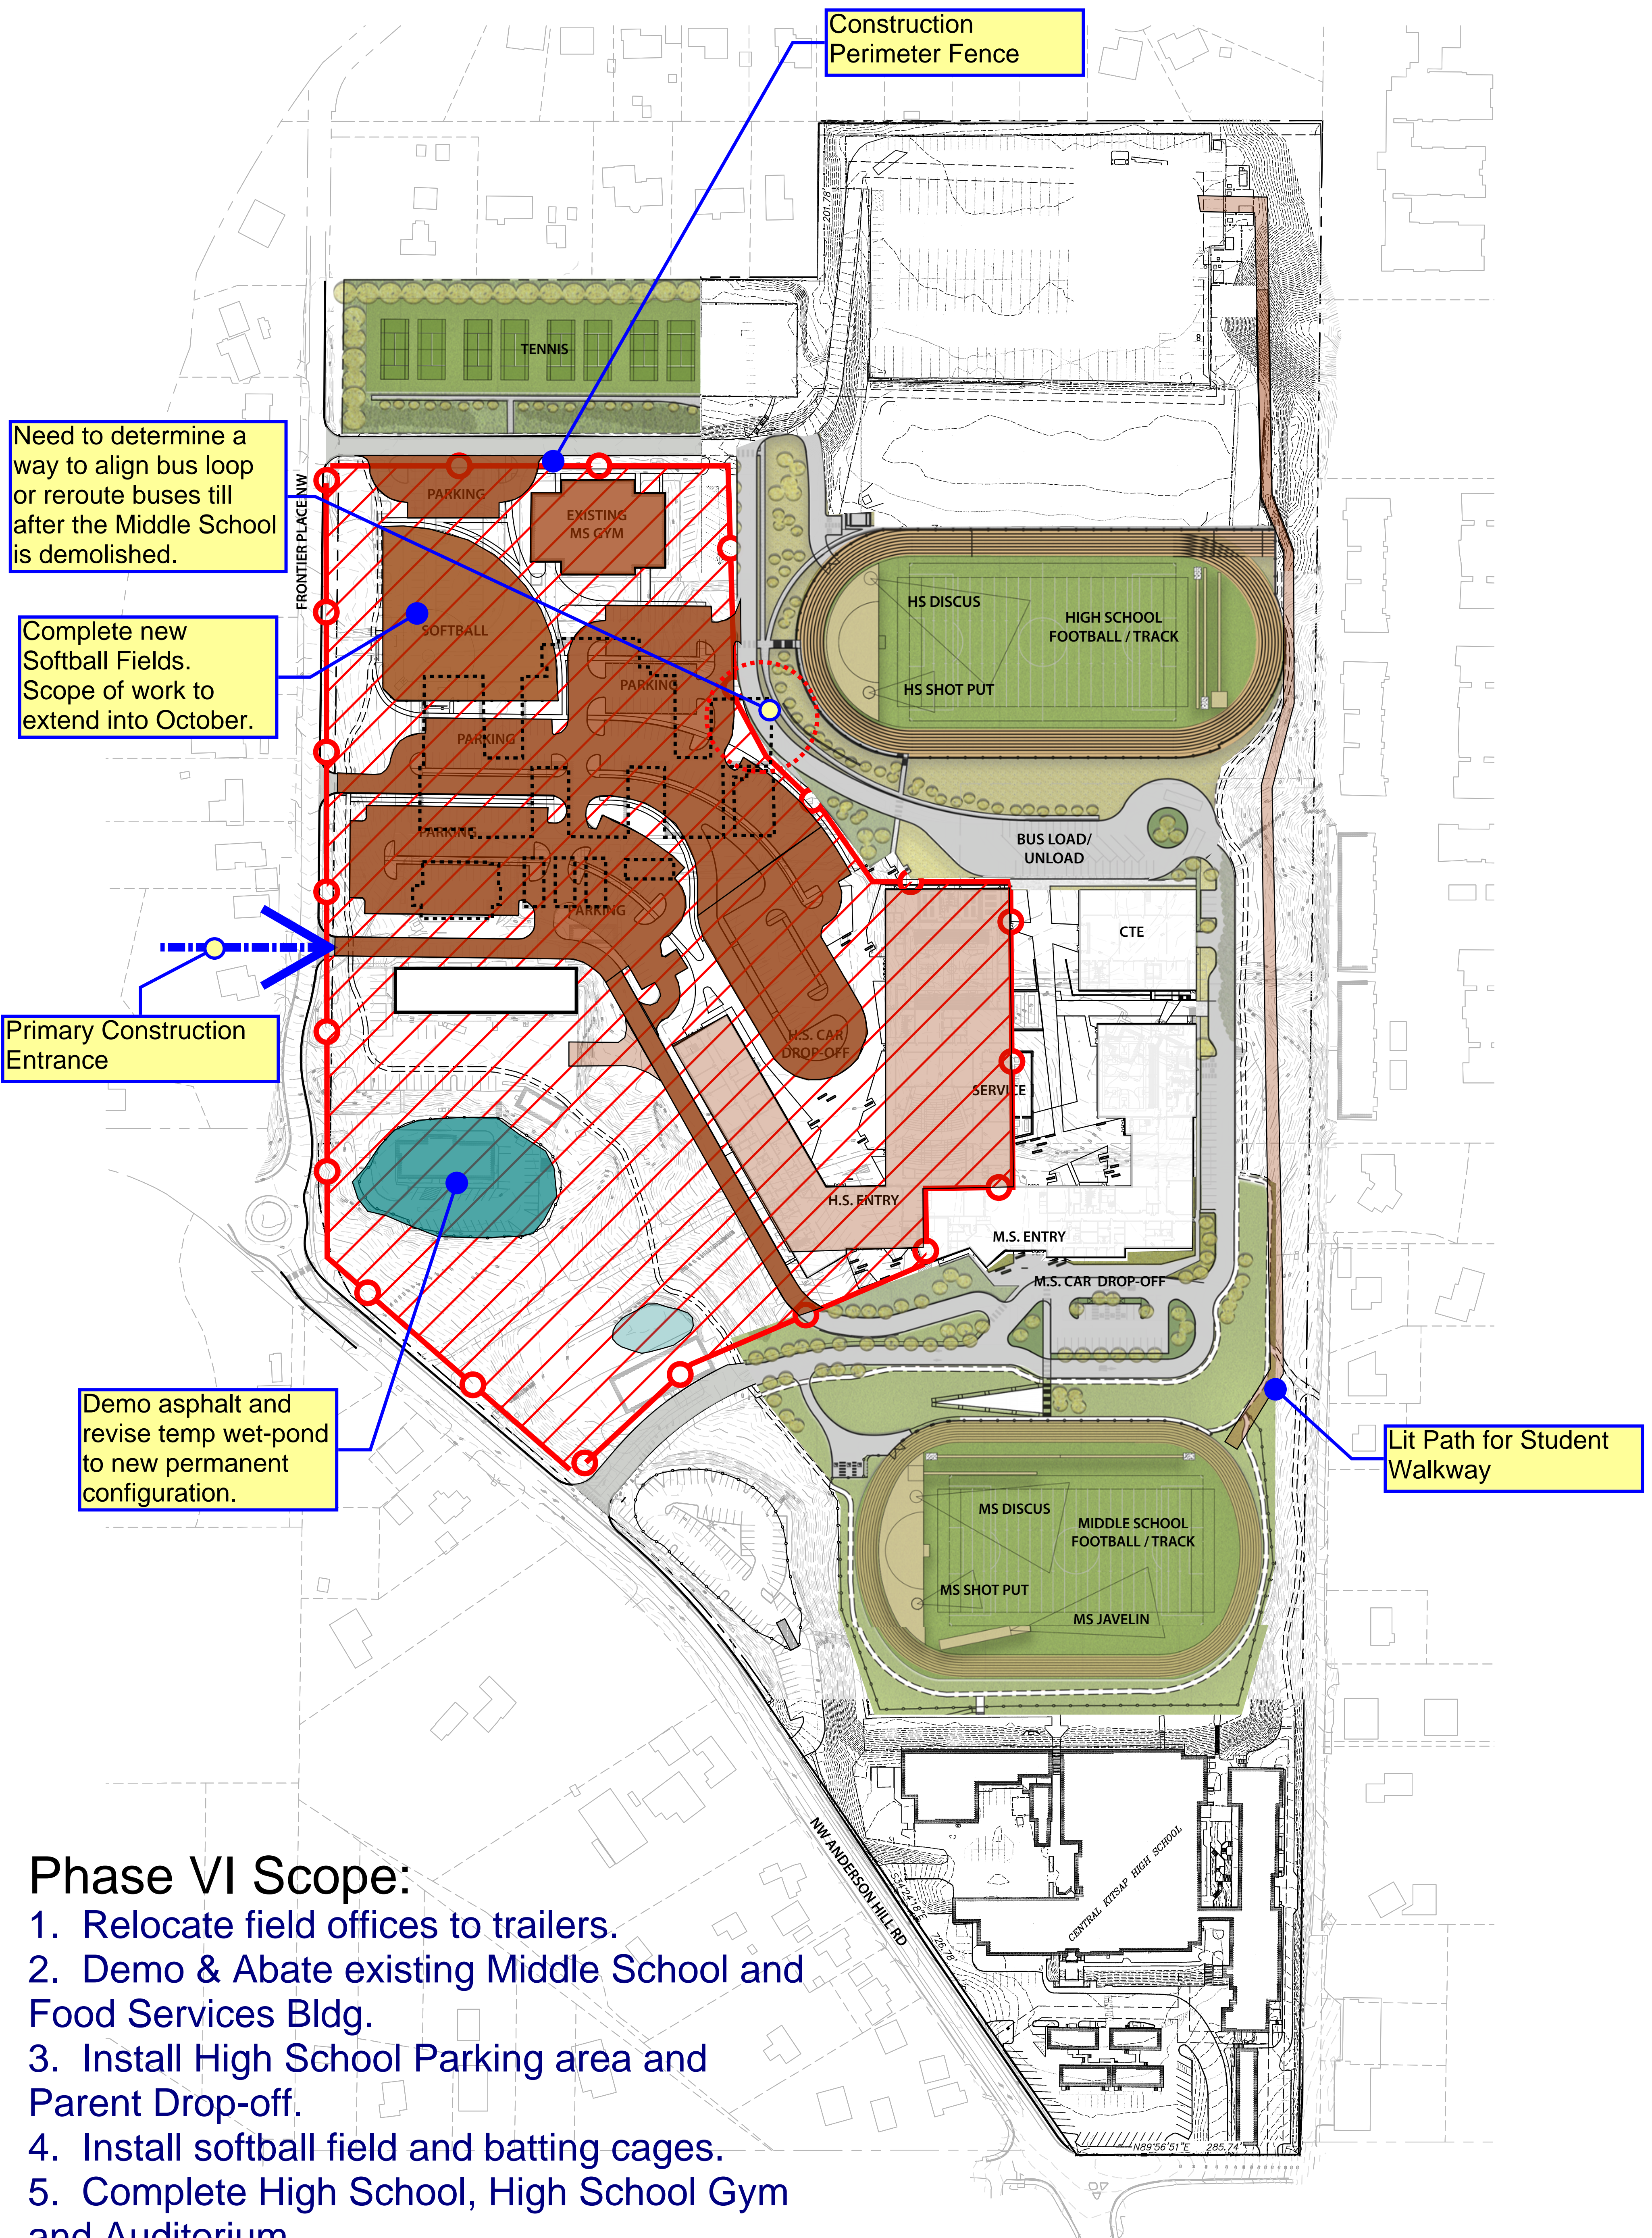

Phase VI Scope:

1. Relocate field offices to trailers.
2. Demo & Abate existing Middle School and Food Services Bldg.
3. Install High School Parking area and Parent Drop-off.
4. Install softball field and batting cages.
5. Complete High School, High School Gym and Auditorium.

PHASE VI
 Jan. 2019 - June 2019

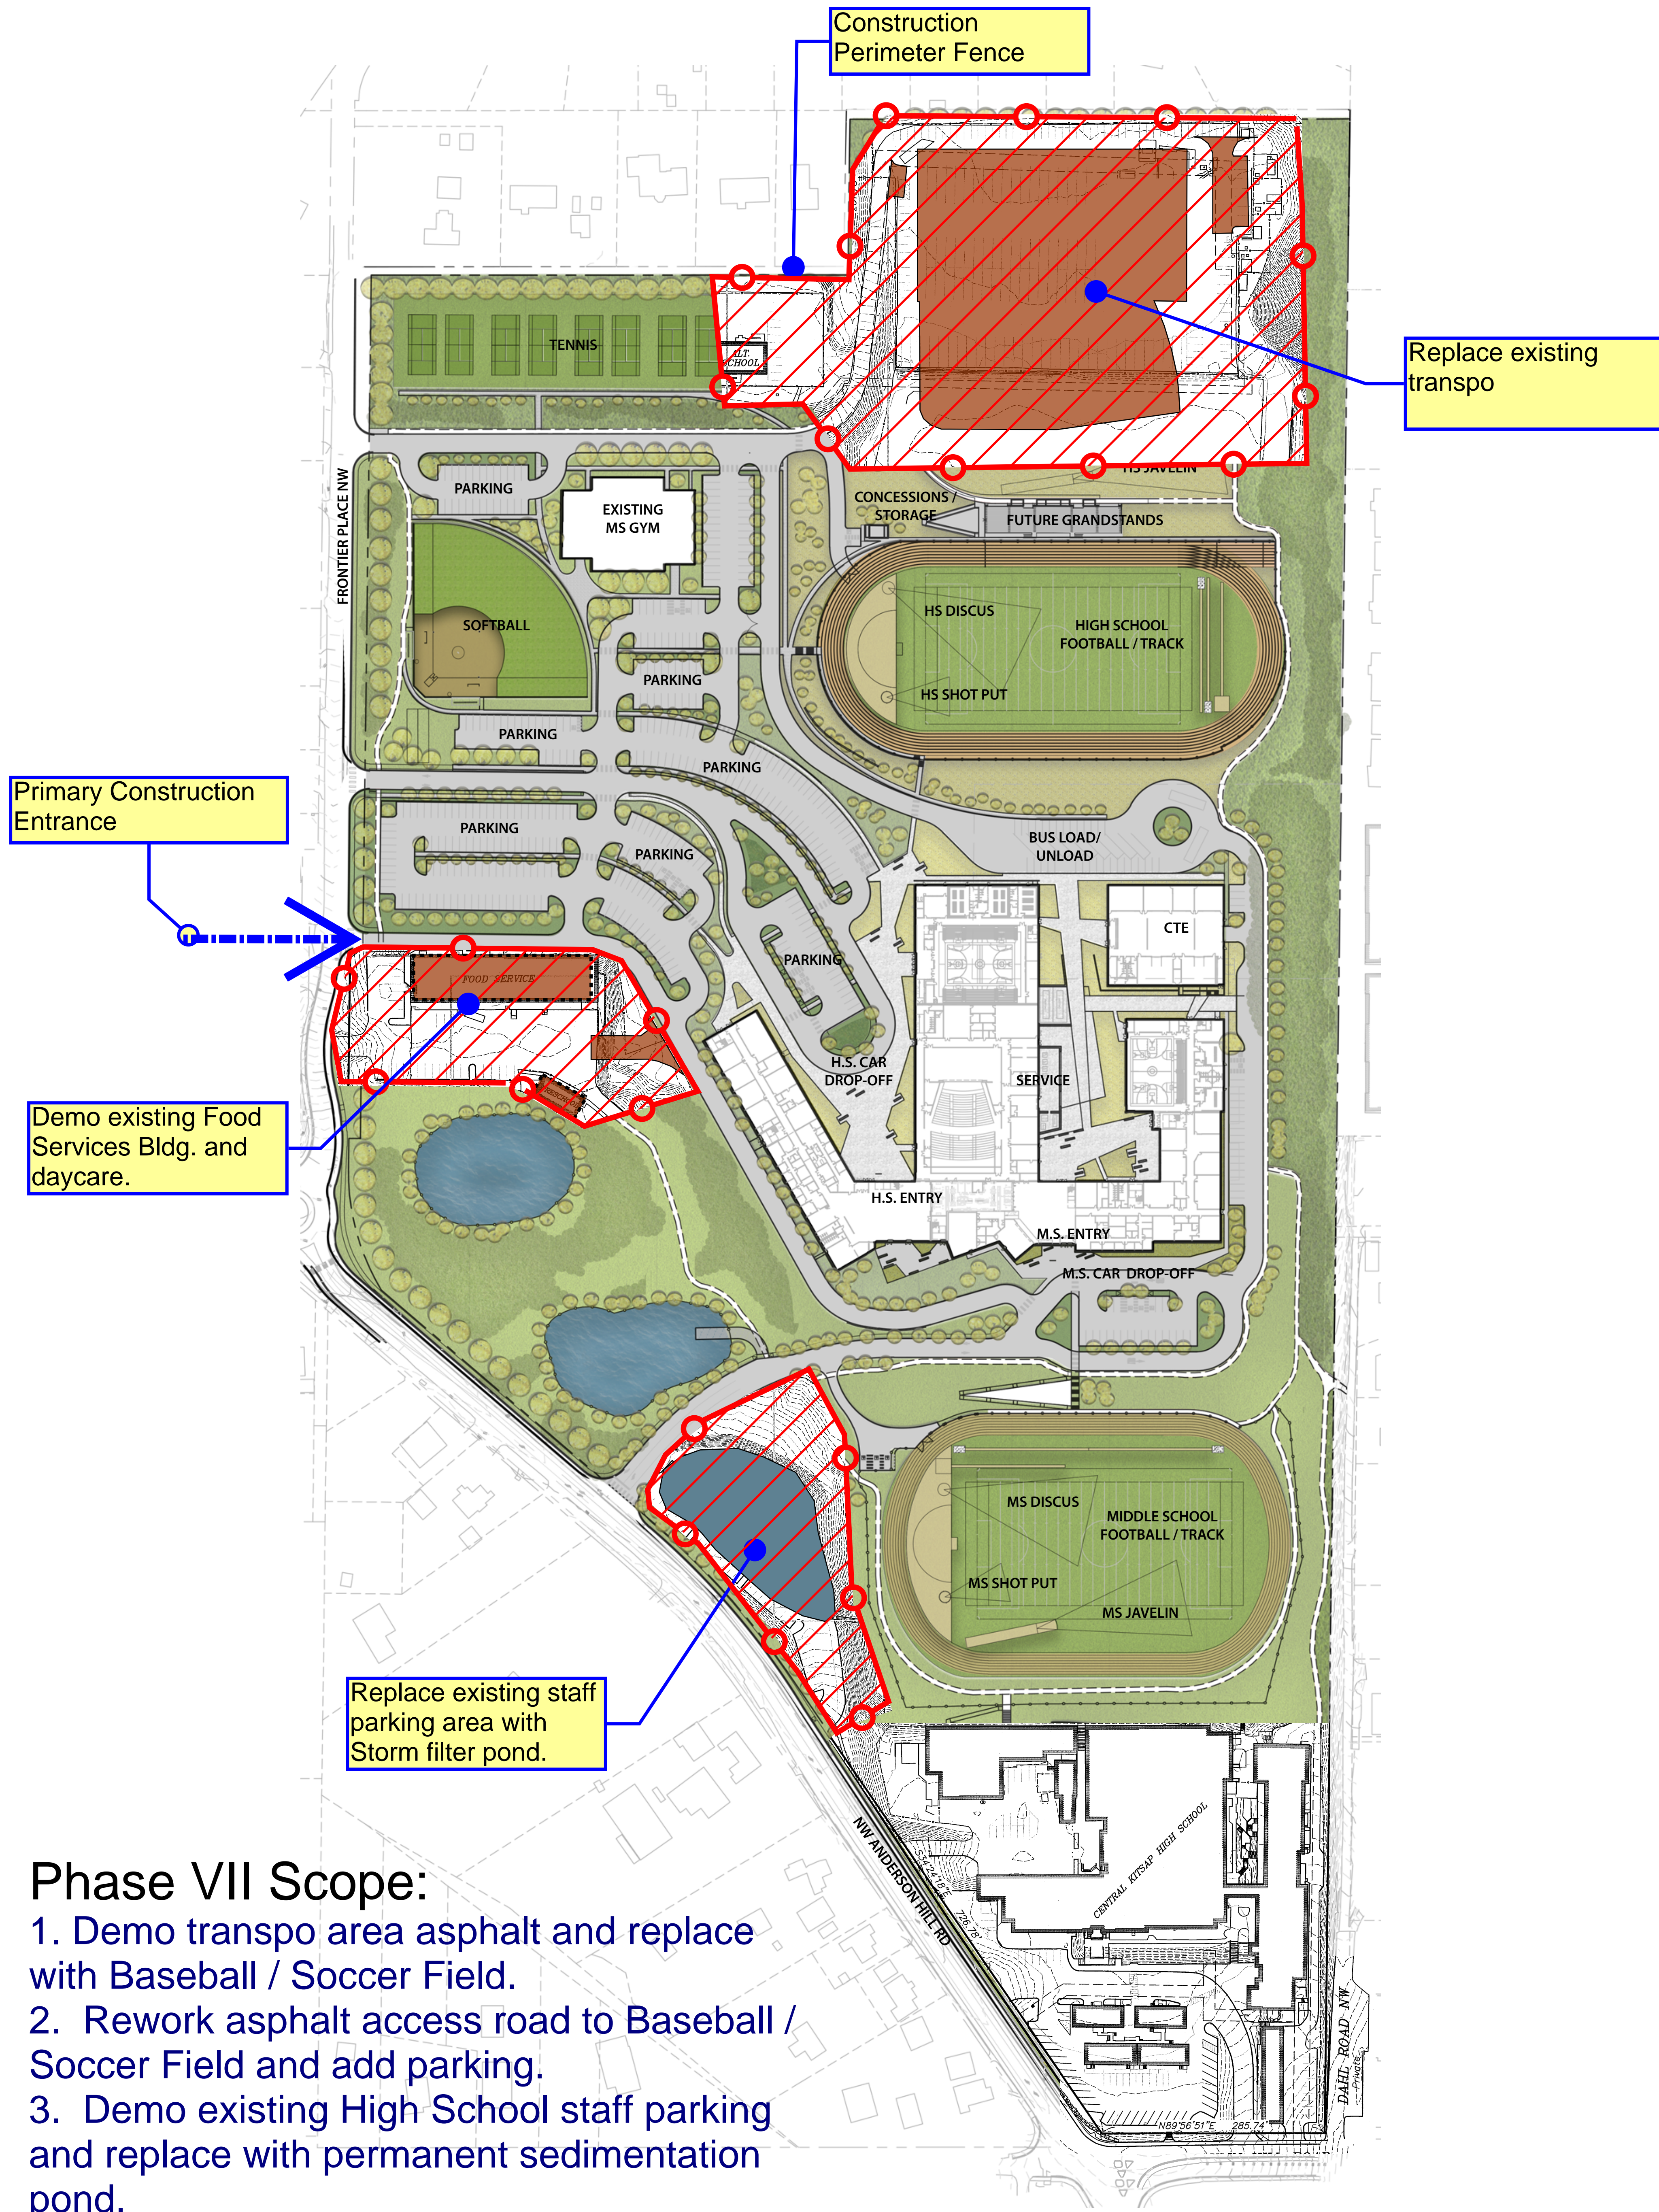

Phase VII Scope:

- 1. Demo transpo area asphalt and replace with Baseball / Soccer Field.
- 2. Rework asphalt access road to Baseball / Soccer Field and add parking.
- 3. Demo existing High School staff parking and replace with permanent sedimentation pond.

PHASE VII
 July 2019 - August. 2019

